

Project No.: **YORKX22001**

Report Date: **June 11, 2025**

Project Name: **York Building Products**

Date Received: **June 11, 2024**

Laboratory Number: **208189**

Client: **York Building Products**

Address: **Sam Cooke**

950 Smile Way

York, PA 17404

Unit Specification: **ASTM C1372**


Unit Designation and

Description: **Segmental Retaining Wall Unit**
Compac III SRW - Frederick Plan

Testing conducted in: **Water**

Summary of Test Results

Specimen No.	% Loss - Final Oven Dry Basis							
	20	40	60	80	100	120	140	150
1	0.00	0.01	0.02	0.03	0.04	0.04	0.04	0.04
2	0.01	0.01	0.02	0.03	0.04	0.04	0.04	0.04
3	0.01	0.02	0.02	0.04	0.06	0.06	0.06	0.06
4	0.01	0.01	0.01	0.03	0.04	0.04	0.04	0.04
5	0.00	0.02	0.02	0.10	0.14	0.14	0.14	0.14
Average	0.01	0.01	0.02	0.05	0.06	0.06	0.06	0.06

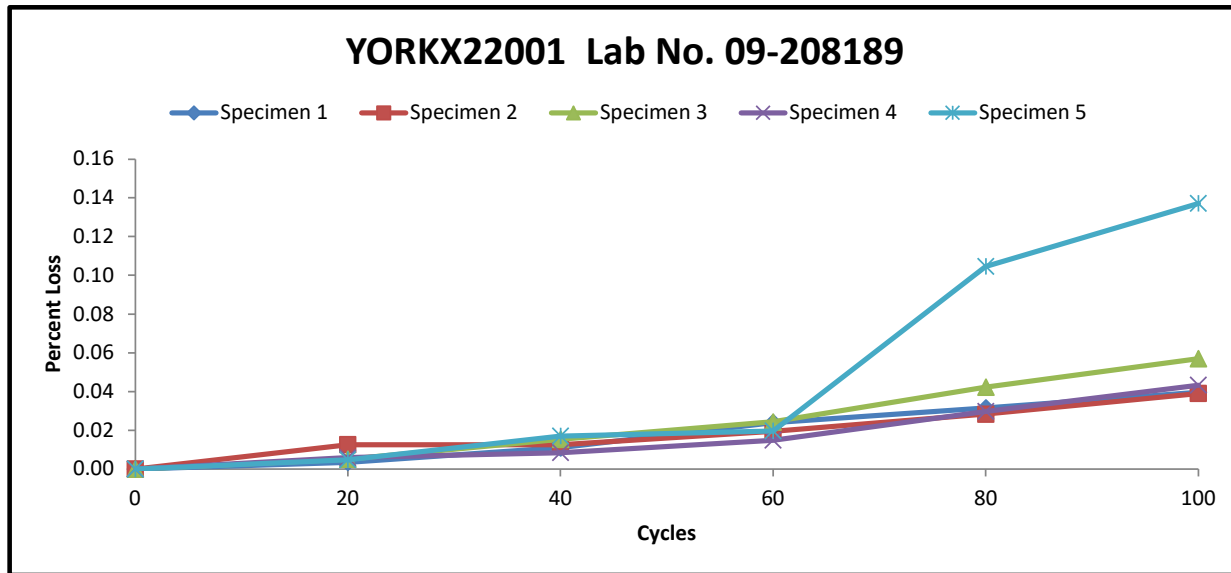

Remarks: The units were tested according to ASTM C1262. This set meets the freeze-thaw requirement of ASTM C1372.

Joseph Ridgway, P.E.
Laboratory Manager

Laboratory Photographs

